



# Arlington High School Building Project

AHS Construction Update – 9/10/20

## Arlington HS Construction Schedule: April 2020 – April 2025

### Construction Details

Phase 1 site-work and temporary phasing is nearing completion. Foundations are now underway for the new Phase 1 Building. Work areas during this phase include the front green, the Peirce practice field and the current softball field. Construction work hours will be Monday through Friday will and follow local bylaws (8 AM – 6 PM). Saturday work may be required to maintain the schedule. Material deliveries and other work will be coordinated around the school and traffic schedules to create as little disruption as possible.

### COVID-19 Update

The health and safety of the community and workers on-site are of the highest priority and were taken into consideration in all project-related decisions. Per Governor Baker's announcement, construction work is deemed 'essential' and can continue. For the school to be completed on time, it is very important to maintain the original construction timeline as closely as possible. The construction team will also be maximizing the schedule as students are off-site during this time. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

Sign up for Weekly Construction Updates

<https://ahsbuilding.org/news/construction-updates/>

For more information, visit:

[www.ahsbuilding.org](http://www.ahsbuilding.org)


Email questions or concerns to:

[ahsbuilding@arlington.k12.ma.us](mailto:ahsbuilding@arlington.k12.ma.us)

**For immediate, on-site assistance contact Hal Raymond, Skanska Site Representative, (617) 352-8593**



### PHASE 1 BUILDING CONSTRUCTION (September 2020 – February 2022)

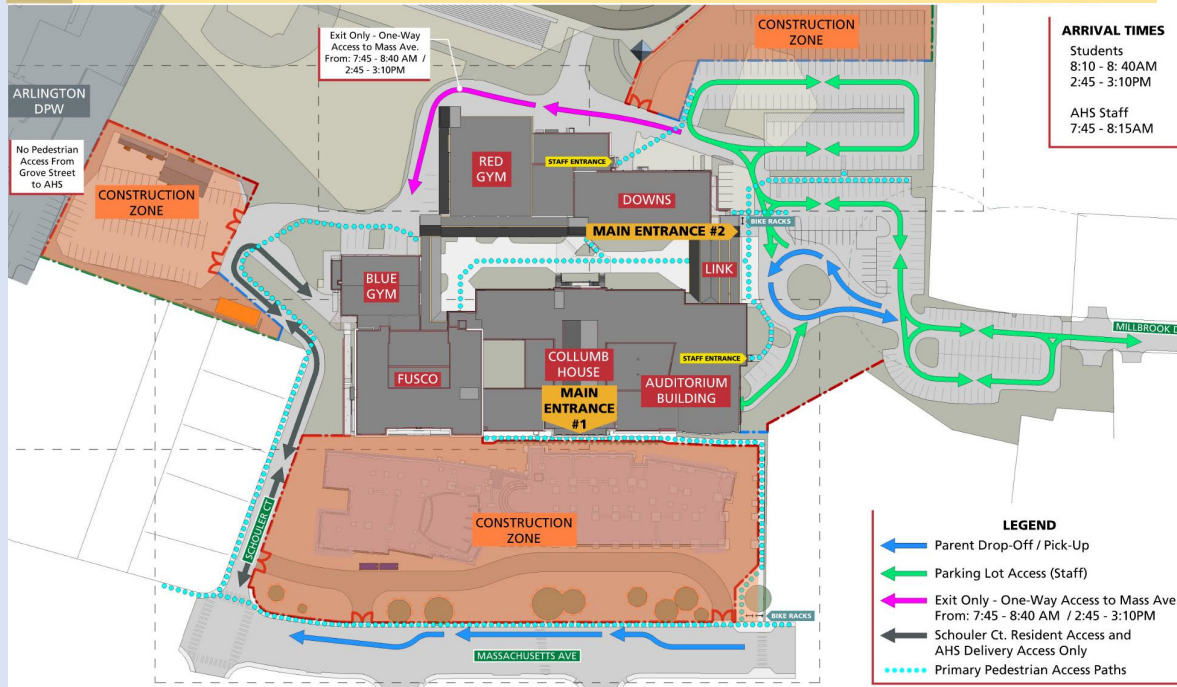

### Construction Look Ahead – Week of September 14, 2020

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

#### Public Way Impacts

- Mass Ave circular drive closed

#### General Site Activities

- Mass Ave Front Lawn:
  - Main Entrance #1 pedestrian covered sidewalk preparation
  - Installation of foundation walls for Phase 1 Building
  - Soil screening and grading
- West Parking Lot:
  - Construction trailers and contractor parking
  - Trenching for installation for electric and telecom services
- Material Stockpile/Temp Construction Lot:
  - Contractor storage and parking
- Schouler Court:
  - Construction vehicles entering and exiting project site

#### Weekend Work/Work Hours

- No weekend work at this time
- Work hours temporarily extended 8:00 am – 6:00 pm (in accordance with local bylaws)



Skanska USA Inc.  
Owner's Project Manager



Consigli Construction Co., Inc.  
Construction Manager at Risk



HMFH Architects, Inc.  
Architect



CONSIGLI  
*Est. 1905*

## ARLINGTON HIGH SCHOOL

### WEEKLY UPDATE – WEEK OF SEPTEMBER 14, 2020

#### Progress Photographs – Taken Week of 08/31/2020



*Photograph 1: Pouring concrete for Spread Footings on the East end*



*Photograph 2: Derenzo digging and holes for more spread footings for building*





CONSIGLI  
*Est. 1905*

## ARLINGTON HIGH SCHOOL

### WEEKLY UPDATE – WEEK OF SEPTEMBER 14, 2020



*Photograph 3: Ariel shot of the site from Fusco Building showing Rammed Aggregate Piers (RAP's) drilling*
